Pawtucket School Department
Pawtucket High School - Design and Construction Schedule

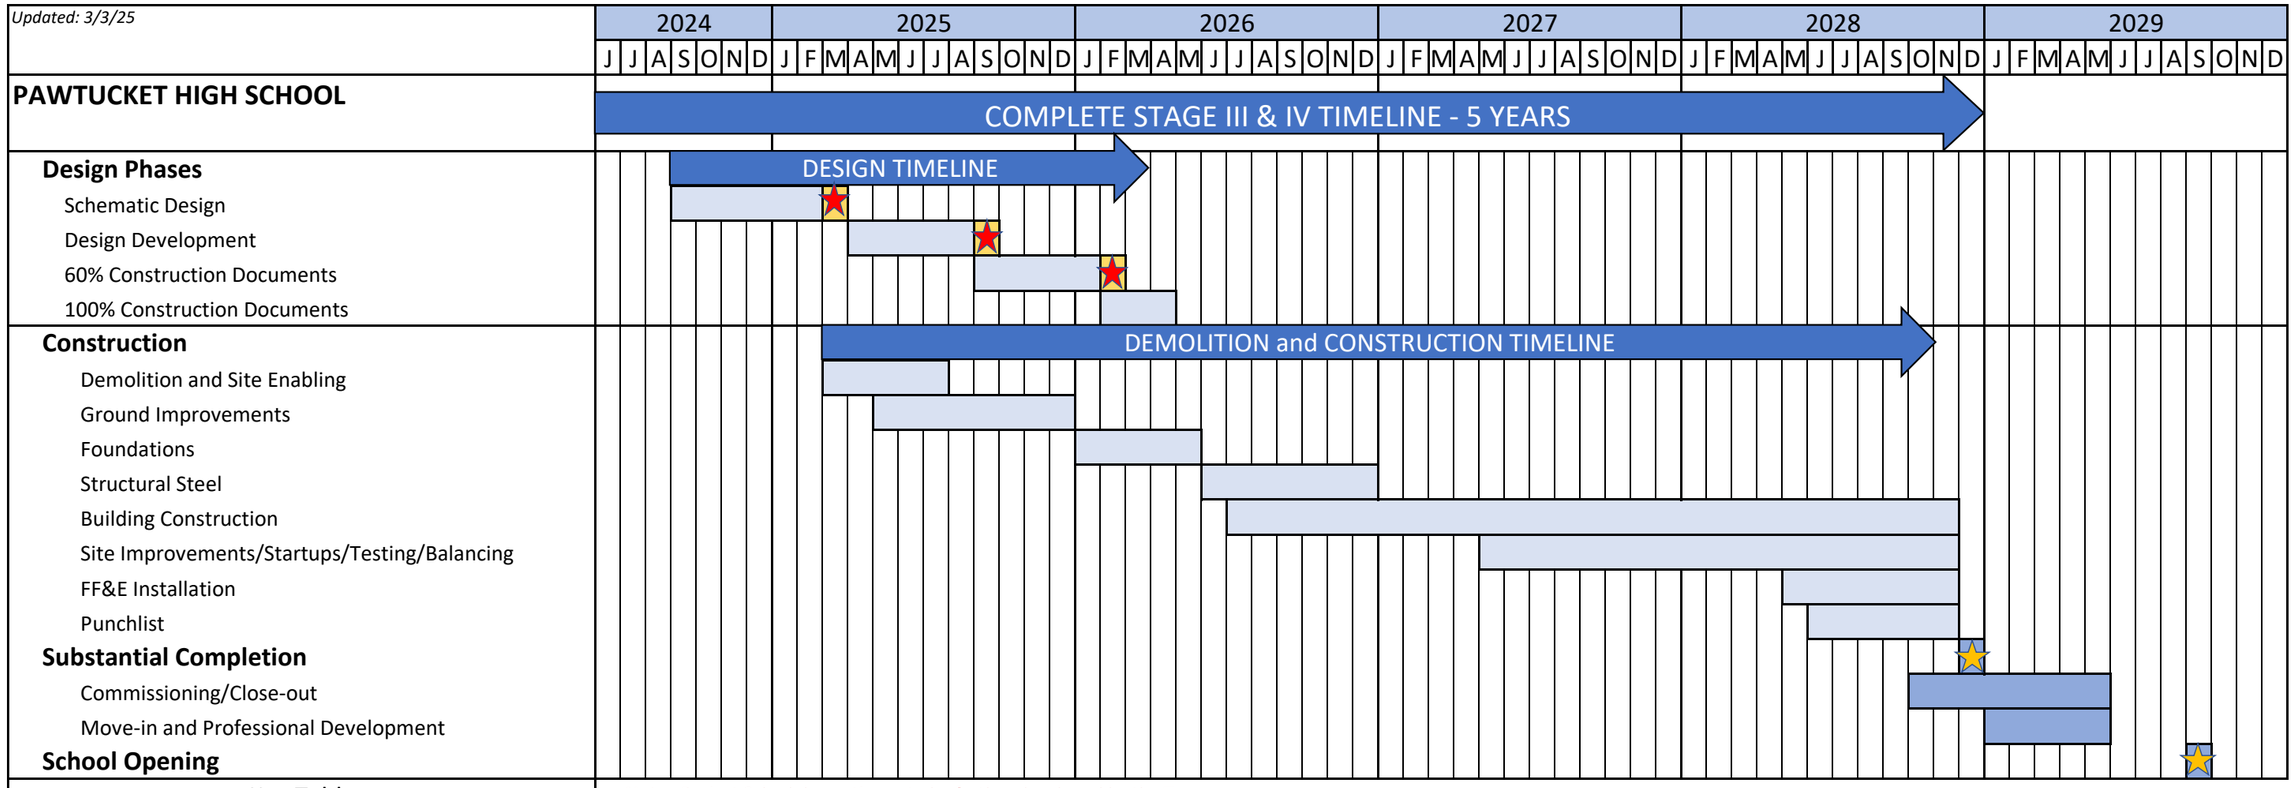

Note: *Project Schedule continues to be further developed by the Team.*

RIDE Rhode Island Department of Education
DLRGROUP Jonathan Levi Architects
SHAWMUT
Colliers Project Leaders

Pawtucket School Department
Pawtucket High School - Design and Construction Schedule
Early Release Package #2 - Ground Improvements

Colliers
Project Leaders

Updated: 3/3/25

	2024							2025											2026											2027											2028											2029										
	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D
PAWTUCKET HIGH SCHOOL	COMPLETE STAGE III & IV TIMELINE - 5 YEARS																																																																		
Design Phases	DESIGN TIMELINE																																																																		
Schematic Design																																																																		
Design Development																																																																		
60% Construction Documents																																																																	
100% Construction Documents																																																																	
Construction Early Release Packages																																																																	
Demolition and Site Enabling (ERP #1)																																																																	
Ground Improvements (ERP #2)																																																																	

	2024							2025											2026											2027											2028											2029										
	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D
Construction	DEMOLITION and CONSTRUCTION TIMELINE																																																																	
Ground Improvements (ERP #2)																																																																	
Mobilization On-site																																																																	
Site Cleanup in Preparation for Work																																																																
Excavation and Production																																																																
Import/Fill/Compact Site																																																															
Complete Ground Improvements																																																															
Foundations																																																																	
Structural Steel																																																															
Building Construction																																																															
Site Improvements/Startups/Testing/Balancing																																																														
FF&E Installation																																																														
Punchlist																																																														
Substantial Completion																																																													
Commissioning/Close-out																																																												
Move-in and Professional Development																																																											
School Opening																																																											

Key Table	
Milestone dates	☆
RIDE Submission dates	★
RIDE Submission Review	
